




PRELIMINARY SCHEDULE

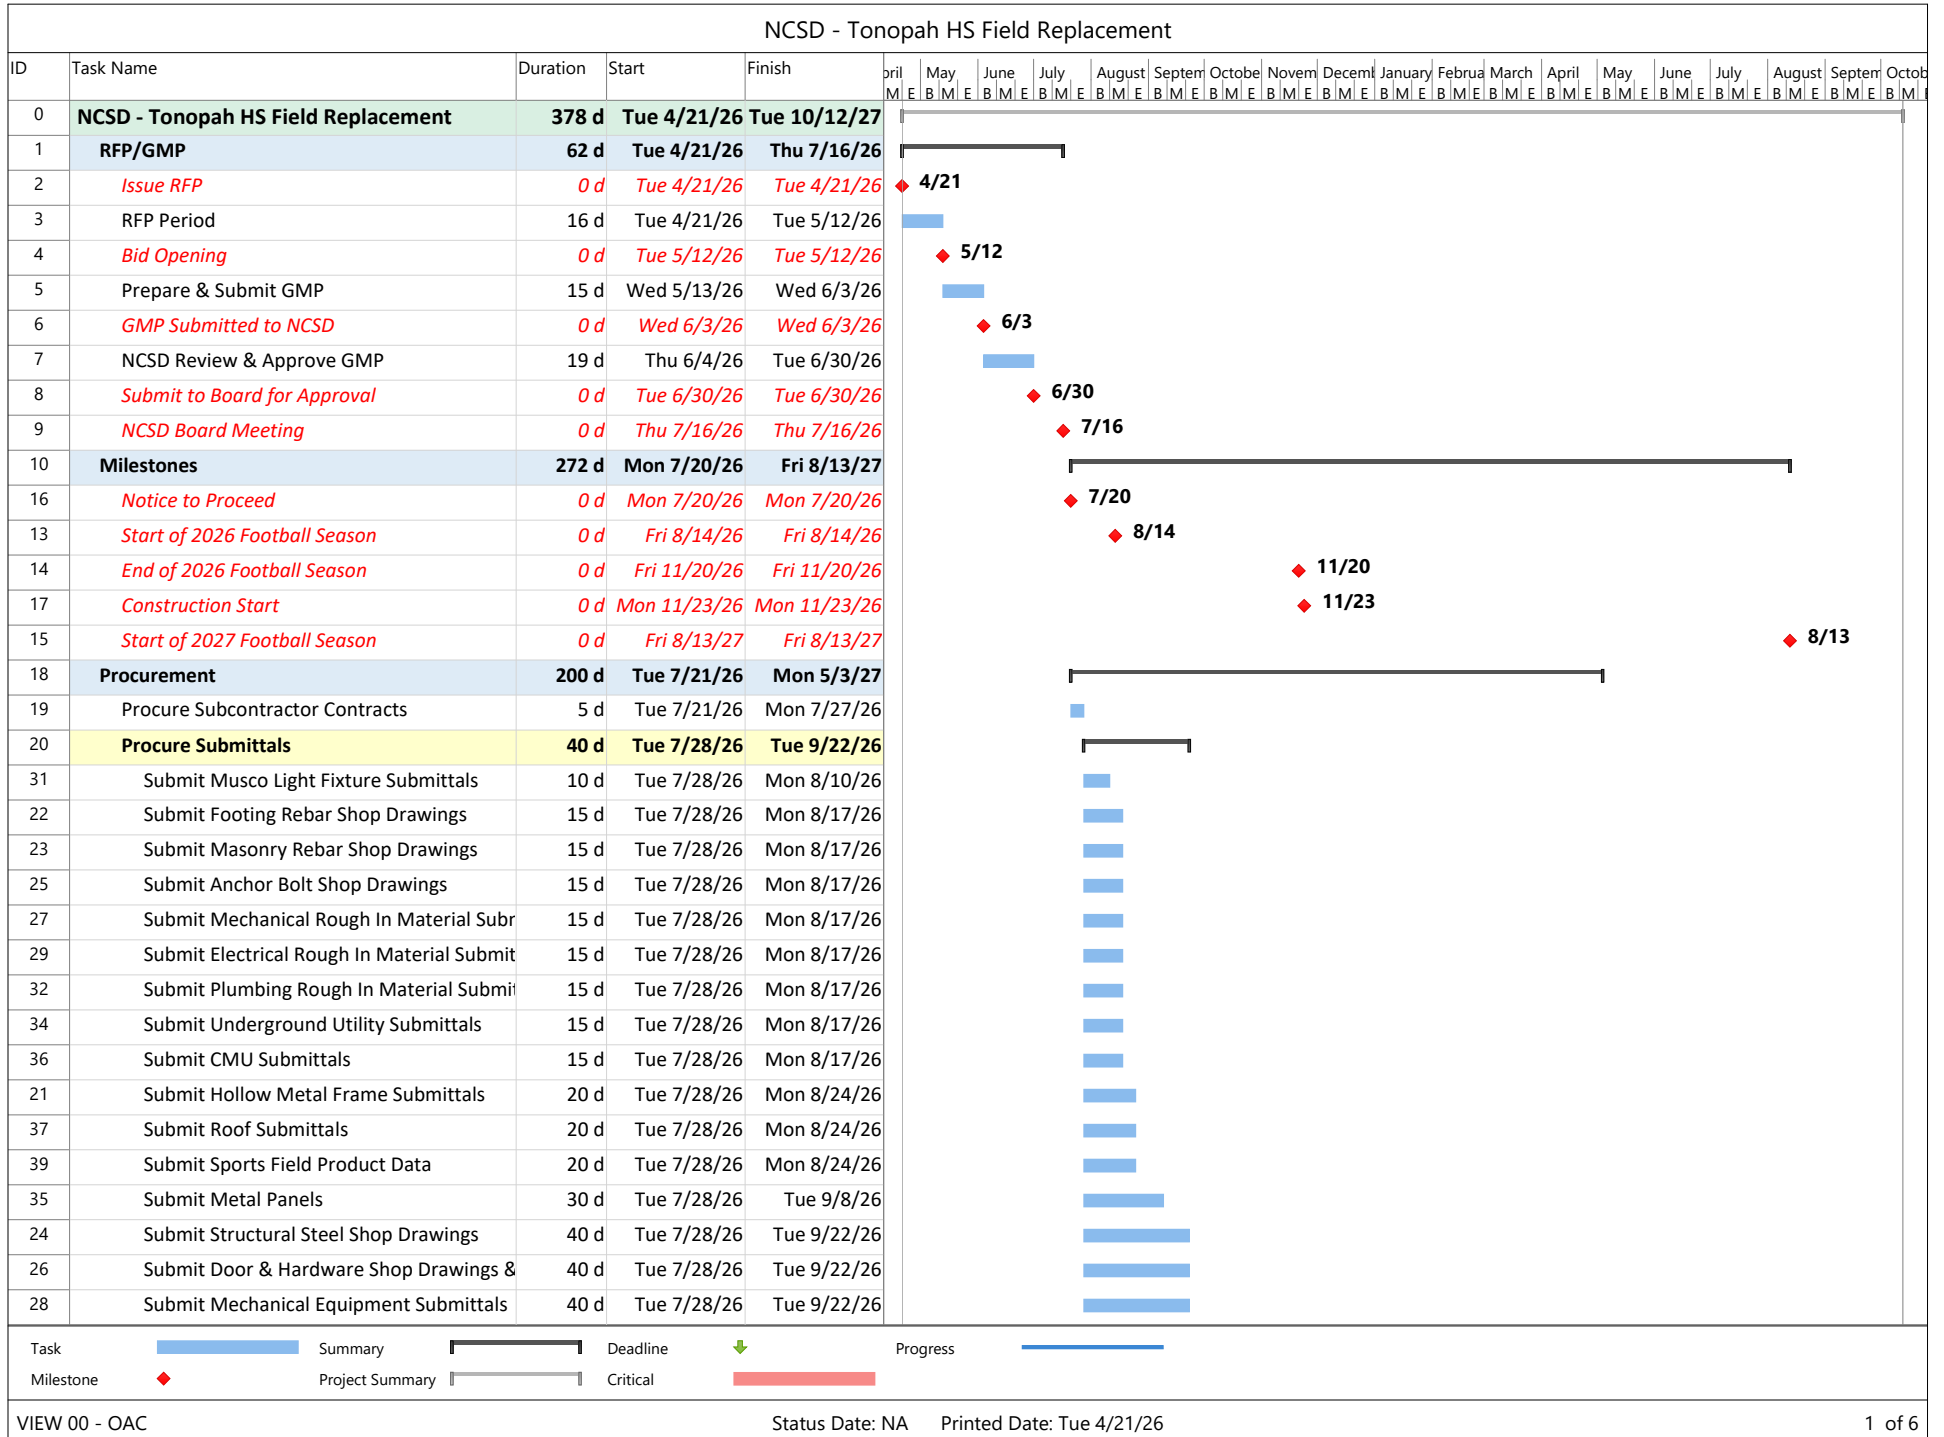


PRELIMINARY SCHEDULE

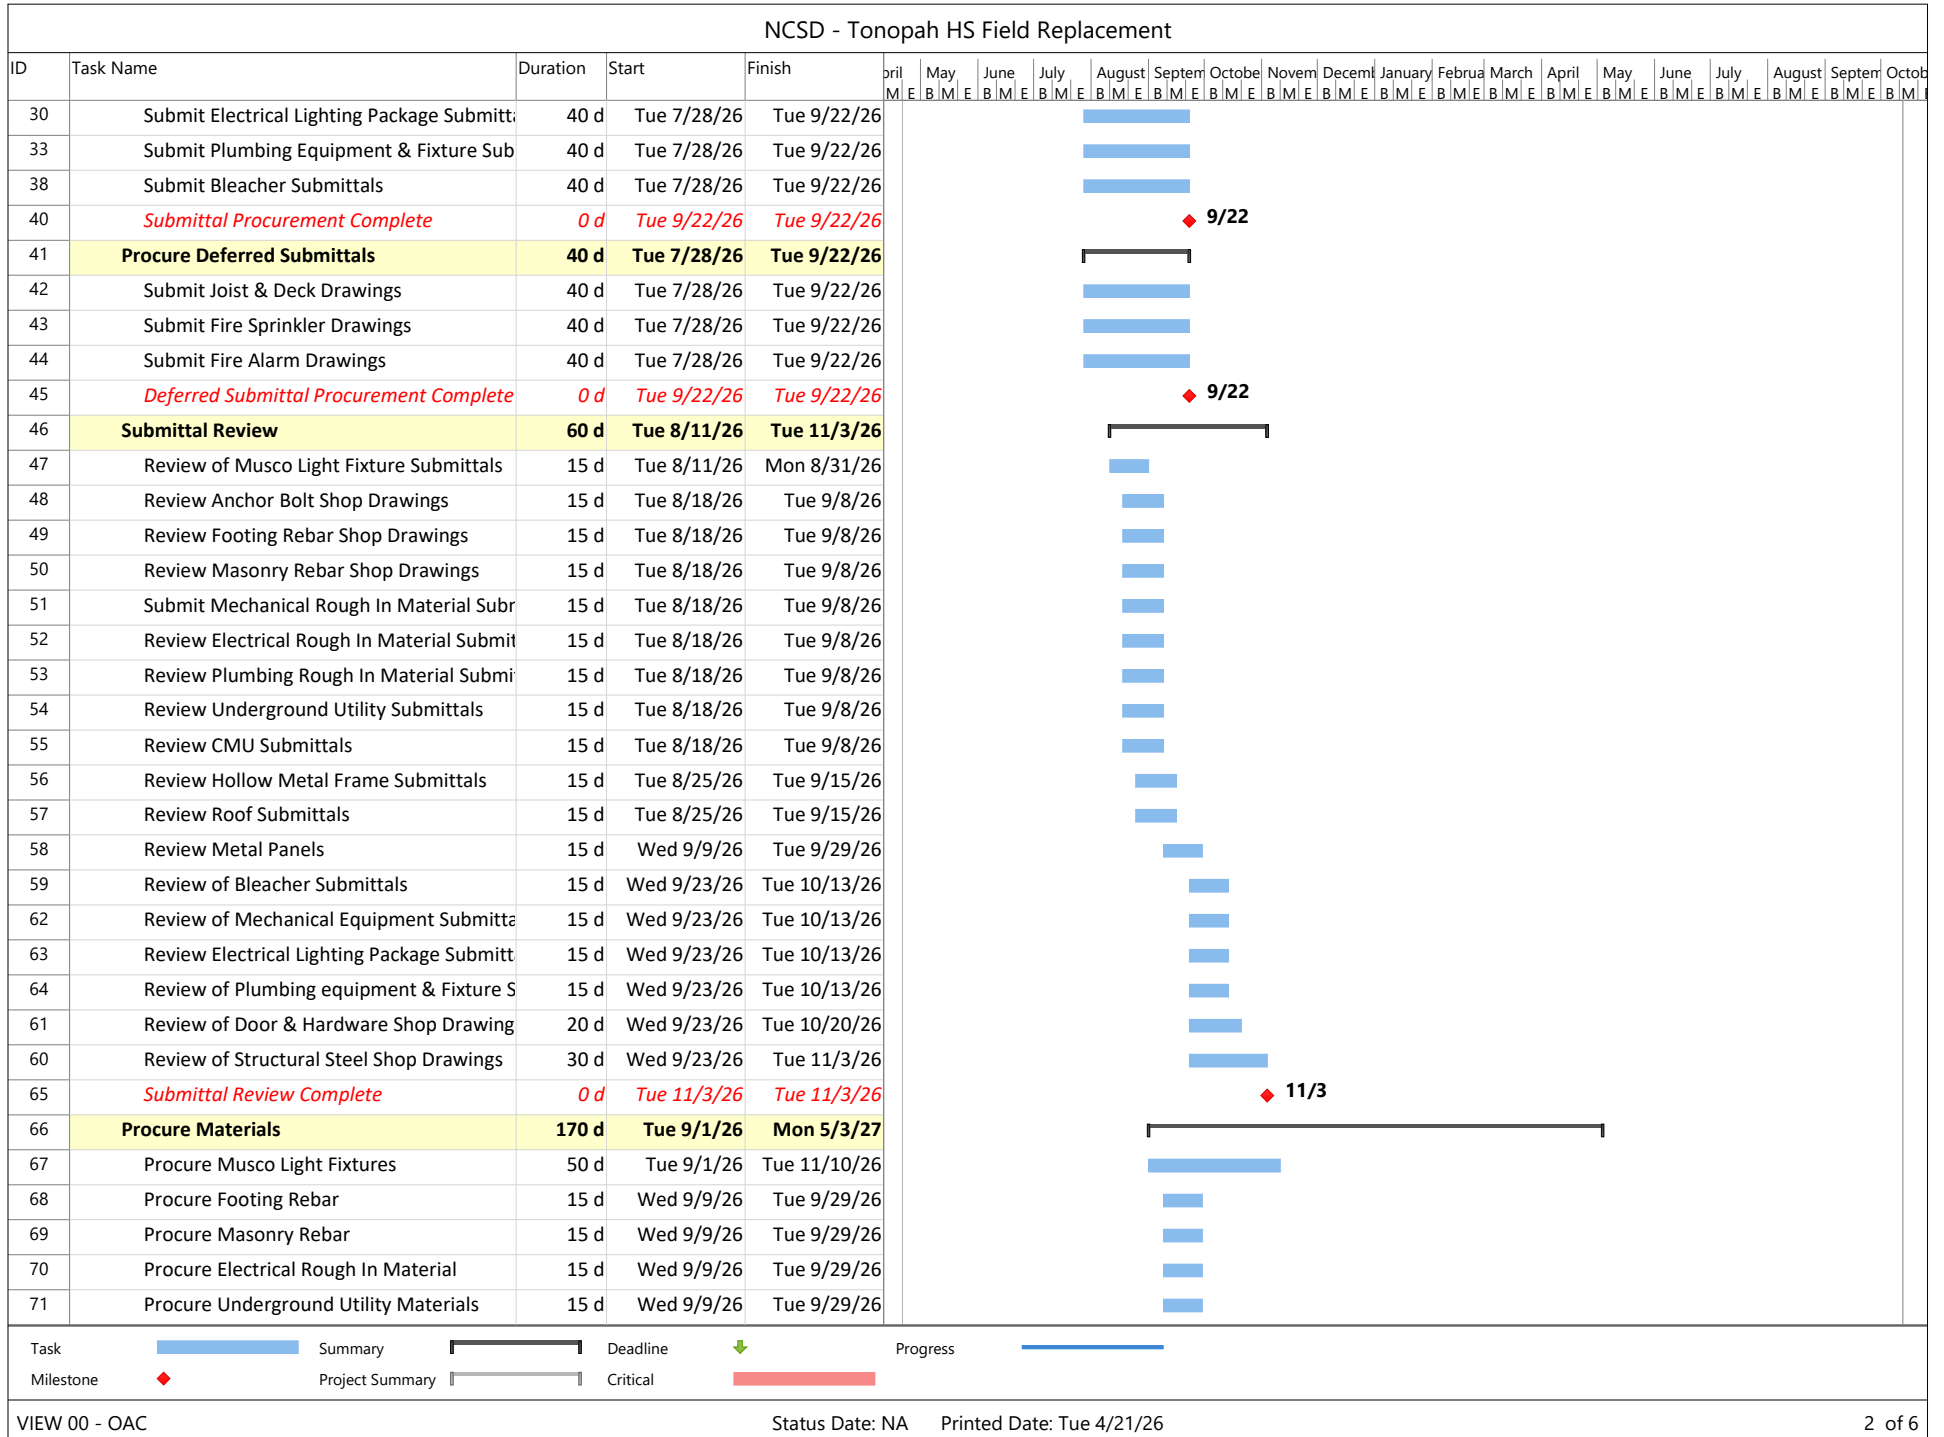

PRELIMINARY SCHEDULE

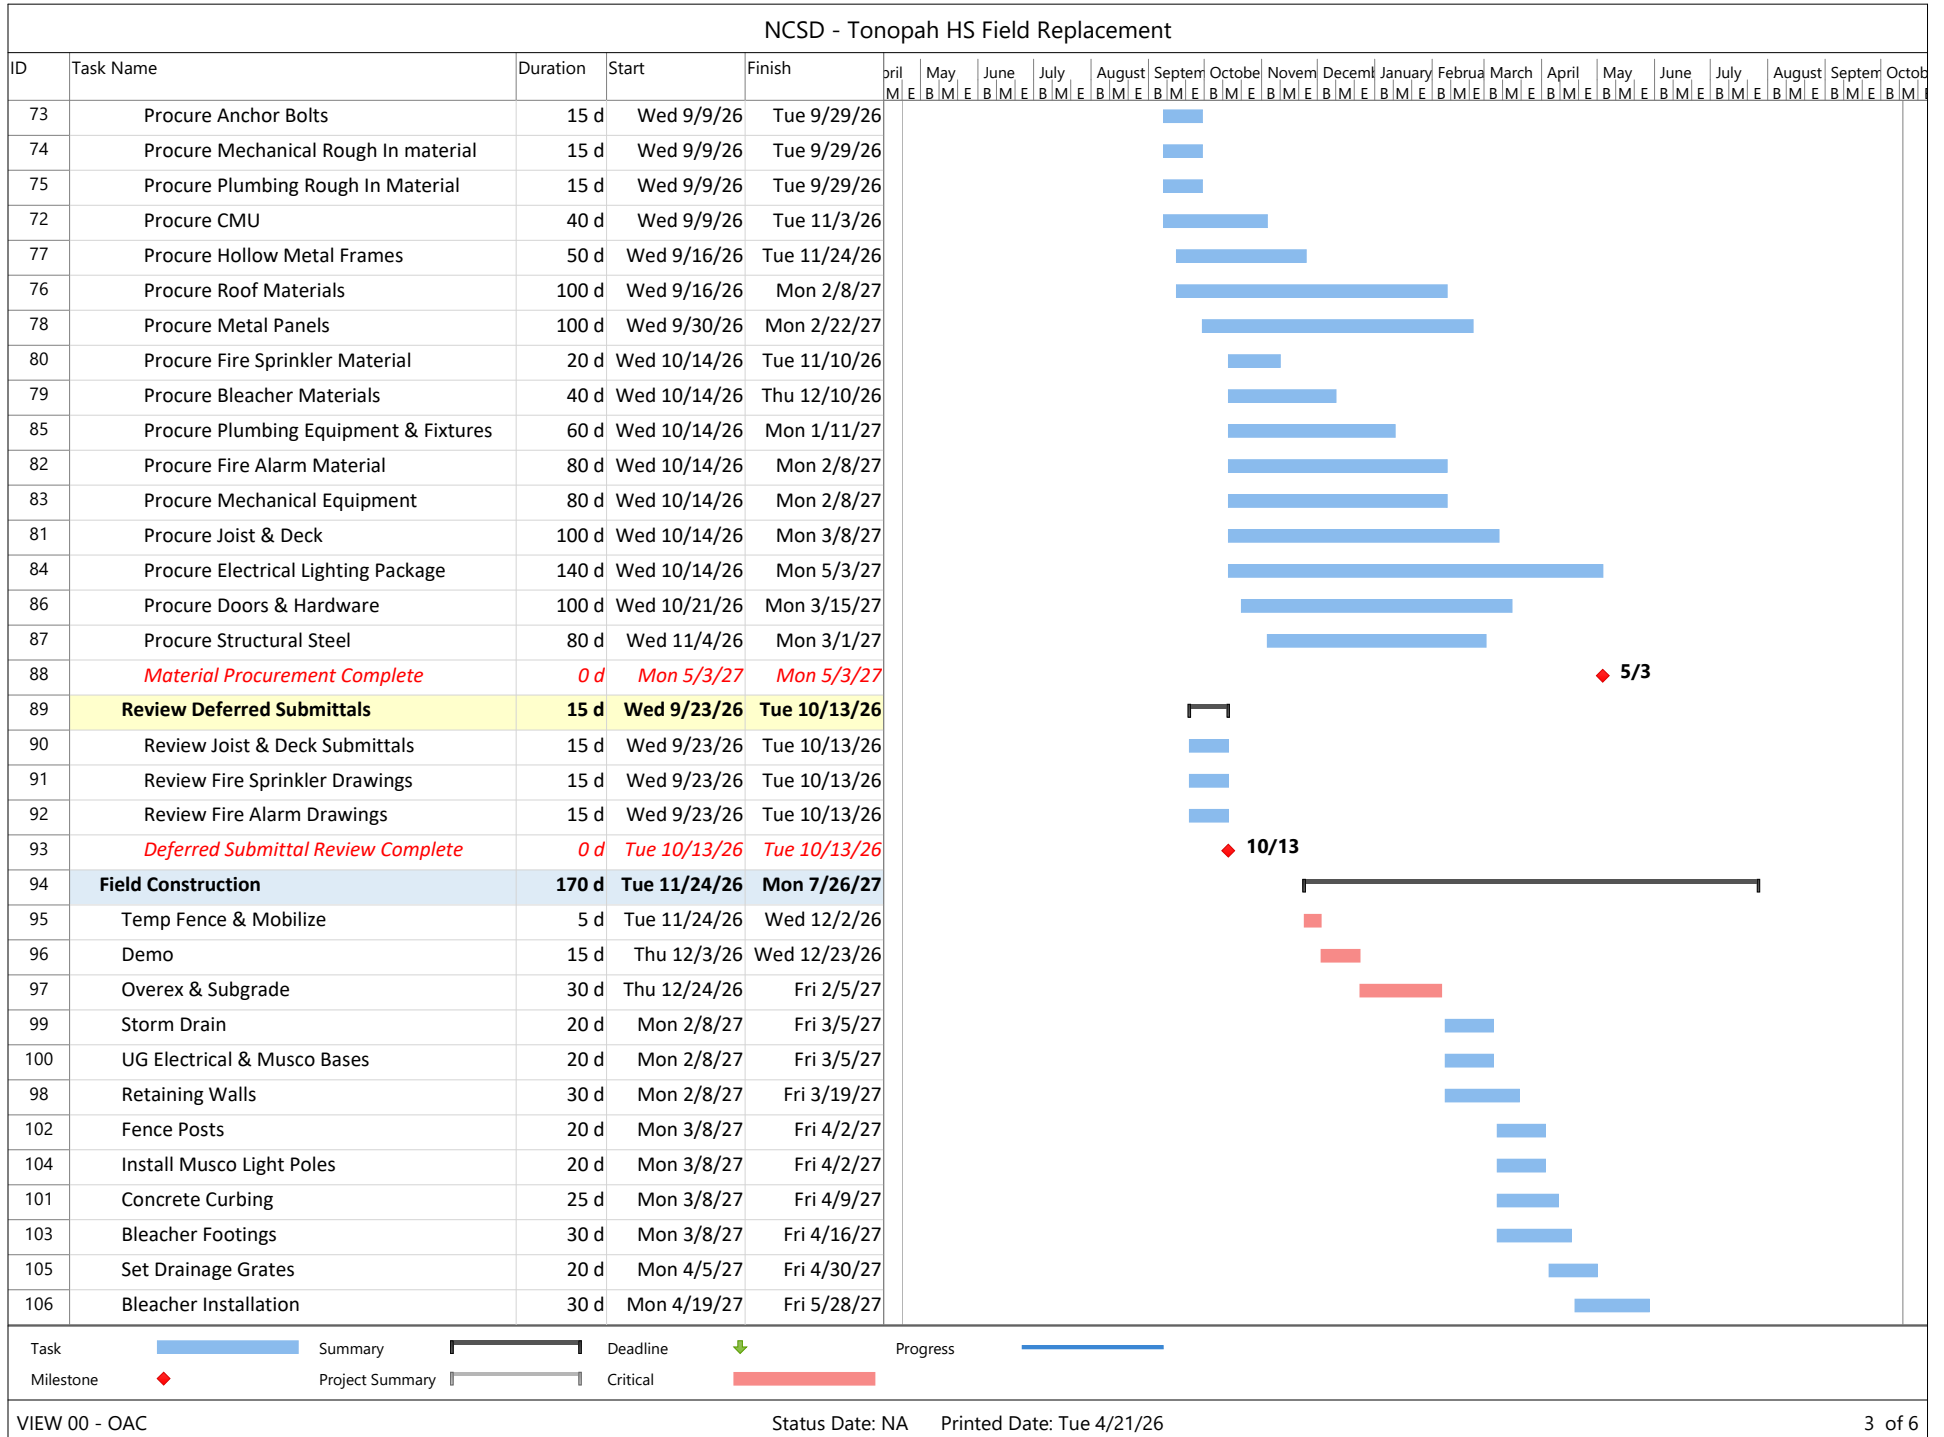

PRELIMINARY SCHEDULE

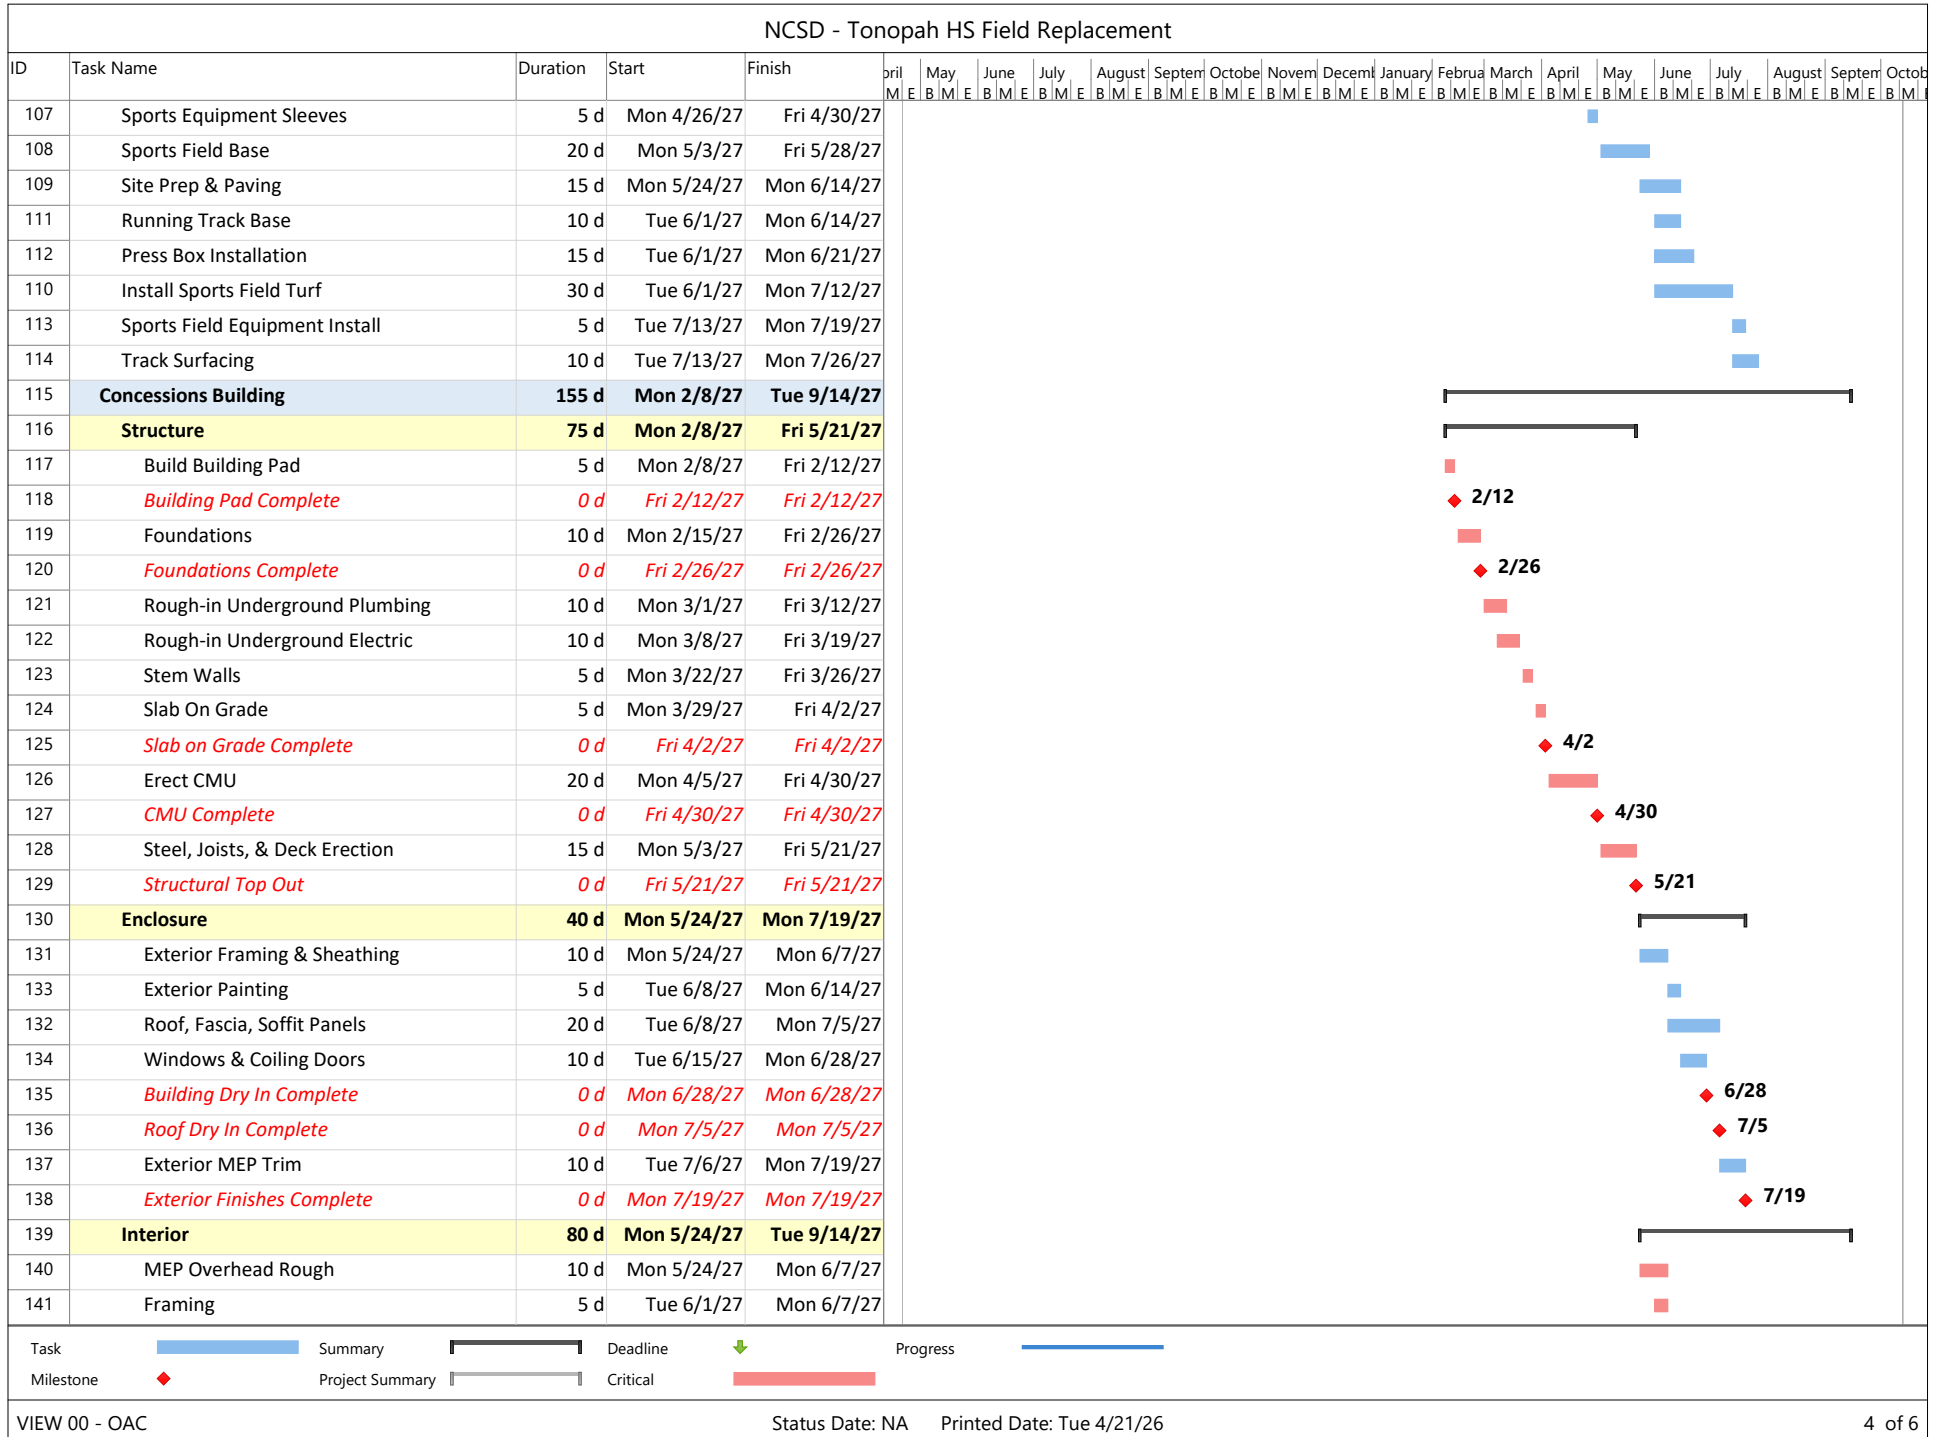

PRELIMINARY SCHEDULE

ID	Task Name	Duration	Start	Finish
142	Framing Complete	0 d	Mon 6/7/27	Mon 6/7/27
143	MEP Rough In Walls	10 d	Tue 6/8/27	Mon 6/21/27
144	MEP Rough-Ins Complete	0 d	Mon 6/21/27	Mon 6/21/27
145	Insulation	5 d	Tue 6/22/27	Mon 6/28/27
146	Drywall	5 d	Tue 6/22/27	Mon 6/28/27
147	Tape & Texture	10 d	Fri 6/25/27	Thu 7/8/27
148	Drywall Complete	0 d	Mon 6/28/27	Mon 6/28/27
149	Paint	5 d	Tue 7/6/27	Mon 7/12/27
150	Interior Paint Complete	0 d	Mon 7/12/27	Mon 7/12/27
151	Casework	5 d	Tue 7/13/27	Mon 7/19/27
152	MEP Trim	10 d	Tue 7/20/27	Mon 8/2/27
153	Flooring	10 d	Tue 8/3/27	Mon 8/16/27
154	Flooring Complete	0 d	Mon 8/16/27	Mon 8/16/27
155	Doors & Hardware	5 d	Tue 8/17/27	Mon 8/23/27
156	Construction Clean	2 d	Tue 8/24/27	Wed 8/25/27
157	Pre-Punch	10 d	Thu 8/26/27	Thu 9/9/27
158	Final Clean	2 d	Fri 9/10/27	Mon 9/13/27
159	Create Punch List	1 d	Tue 9/14/27	Tue 9/14/27
160	Building Systems	45 d	Tue 7/6/27	Tue 9/7/27
161	Set Electrical Equipment	5 d	Tue 7/6/27	Mon 7/12/27
162	Set Mechanical Equipment	5 d	Tue 7/13/27	Mon 7/19/27
163	Electric Single Line	10 d	Tue 7/13/27	Mon 7/26/27
164	Permanent Power Complete	0 d	Mon 7/26/27	Mon 7/26/27
165	HVAC Start Up	10 d	Tue 7/27/27	Mon 8/9/27
166	Building Climatized	0 d	Mon 8/9/27	Mon 8/9/27
167	Test and Balance	10 d	Tue 8/24/27	Tue 9/7/27
168	Sports Field Substantial Completion	0 d	Mon 7/26/27	Mon 7/26/27
169	Concession Building Substantial Completion	0 d	Tue 9/14/27	Tue 9/14/27
170	Contractual Substantial Completion	0 d	Tue 9/14/27	Tue 9/14/27
171	Complete Punch List	10 d	Wed 9/15/27	Tue 9/28/27
172	Contractual Close Out	20 d	Wed 9/15/27	Tue 10/12/27
173	Project Final Completion	0 d	Tue 10/12/27	Tue 10/12/27

Task		Summary		Deadline		Progress	
Milestone		Project Summary		Critical			
