




NCSD - Tonopah HS Field Replacement Project Schedule

ID	Task Name	Duration	Start	Finish	Qtr 2	Qtr 3	Qtr 4	2027 Qtr 1	Qtr 2	Qtr 3	Qtr 4
0	NCSD - Tonopah HS Field Replacement	314 d	Mon 7/20/26	Tue 10/12/27							
10	Milestones	272 d	Mon 7/20/26	Fri 8/13/27							
16	<i>Notice to Proceed</i>	<i>0 d</i>	<i>Mon 7/20/26</i>	<i>Mon 7/20/26</i>							
13	<i>Start of 2026 Football Season</i>	<i>0 d</i>	<i>Fri 8/14/26</i>	<i>Fri 8/14/26</i>							
14	<i>End of 2026 Football Season</i>	<i>0 d</i>	<i>Fri 11/20/26</i>	<i>Fri 11/20/26</i>							
17	<i>Construction Start</i>	<i>0 d</i>	<i>Mon 11/23/26</i>	<i>Mon 11/23/26</i>							
15	<i>Start of 2027 Football Season</i>	<i>0 d</i>	<i>Fri 8/13/27</i>	<i>Fri 8/13/27</i>							
18	Procurement	150 d	Tue 7/21/26	Mon 2/22/27							
115	Field Construction	180 d	Mon 11/23/26	Fri 8/6/27							
152	Concessions Building	166 d	Fri 1/22/27	Tue 9/14/27							
213	<i>Sports Field Substantial Completion</i>	<i>0 d</i>	<i>Fri 8/6/27</i>	<i>Fri 8/6/27</i>							
214	<i>Concession Building Substantial Completion</i>	<i>0 d</i>	<i>Tue 9/14/27</i>	<i>Tue 9/14/27</i>							
215	<i>Contractual Substantial Completion</i>	<i>0 d</i>	<i>Tue 9/14/27</i>	<i>Tue 9/14/27</i>							
216	Complete Punch List	10 d	Wed 9/15/27	Tue 9/28/27							
217	Contractual Close Out	20 d	Wed 9/15/27	Tue 10/12/27							
218	<i>Project Final Completion</i>	<i>0 d</i>	<i>Tue 10/12/27</i>	<i>Tue 10/12/27</i>							

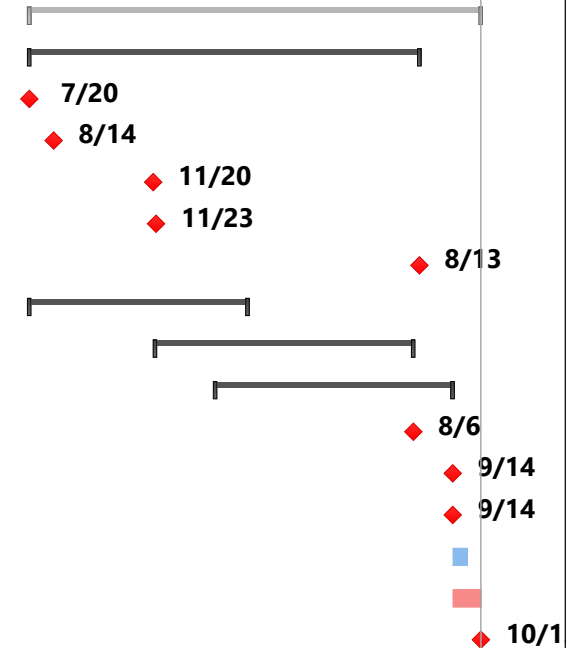

Task Summary Deadline Progress

Milestone Project Summary Critical
